

Document Type: Certificate Of Conformity	Part number: COC-1070.0049	Rev. 02	Rev by: DCADA	Rev. date: 2023-12-14
Product: Baseframe Module	Reviewed by: DROKR	Author: DSOLA	Date: 2018-02-16	

Serial no:

CERTIFICATE OF CONFORMITY	
Customer Technical Purchase Specification No. and Revision	0068-7211 - Latest version
	0069-2093 - Latest version

HydraSpecma Renewables hereby declare these products have been inspected, tested and, unless otherwise is stated below, conform to purchase order and specifications from Customer.

HSRE part no.	Customer part no.	Description
1070.0049	29107156	Baseframe Module

Customer Purchase order:	
Top level Serial number:	1070.0049 -
Manufacturing Order number:	



Work flow:	
Assembled.	According to AI-1071.0512 and AI-1070.0049, Latest revision.
Air leak test.	According to TI-1071.0512-1, Latest revision.
Air fan test	According to TI-1071.0512-2, Latest revision.
Interface dimension for cabinet.	According to TI-1071.0512-3, Latest revision.
Flatness of Baseframe.	According to TI-1071.0512-4, Latest revision.
Pipe system Air leak test or Pipe system Helium leak test.	According to TI-1071.0267, Latest revision. According to TI-1071.0267-1, Latest revision.
Part traceability.	According to SN-1070.0049, Latest revision.
Complete inspection.	Visual inspection of complete unit before packed.
Packing.	According to PI-1070.0049, Latest revision.

Date of Signature	Signature

Document Type: Certificate Of Conformity Appendix	Document: COC-1070.0049-2	Rev. 00	Rev by:	Rev. date: 2023-12-14
Product: Baseframe Module	Reviewed by: DROKR	Author: DSOLA	Date: 2018-02-16	

Serial no :


Appendix B: Measure and control flatness of Baseframe after mounting 3020.0919 into 3020.1212

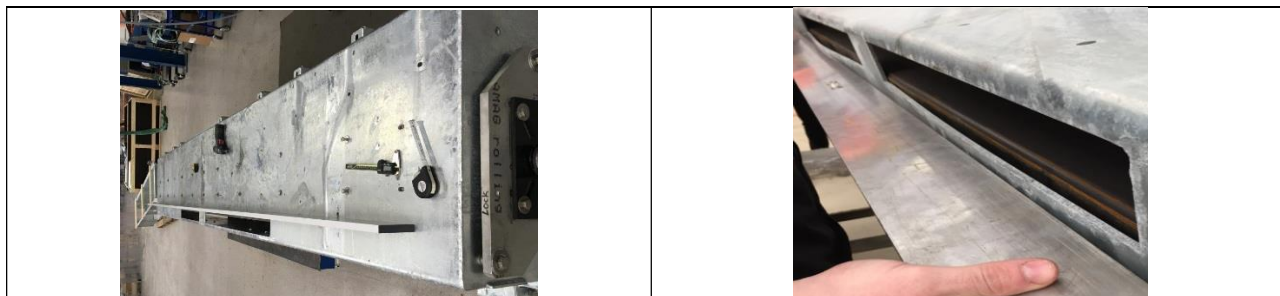

1: Max 4 mm

2: Max 4 mm

3: Max 4 mm

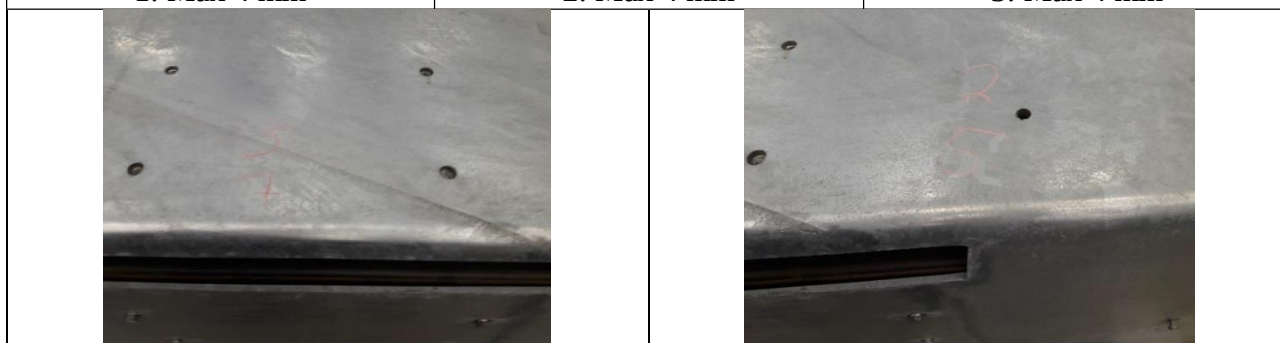

4: Max 4 mm


5: Max 4 mm

1	2	3	4	5

Document Type: Certificate Of Conformity Appendix	Document: COC-1070.0049-1	Rev. 01	Rev by: DCADA	Rev. date: 2023-12-14
Product: Baseframe Module	Reviewed by: DROKR	Author: DSOLA		Date: 2018-02-16

Appendix A.: Interface holes for cabinets.

Serial no:

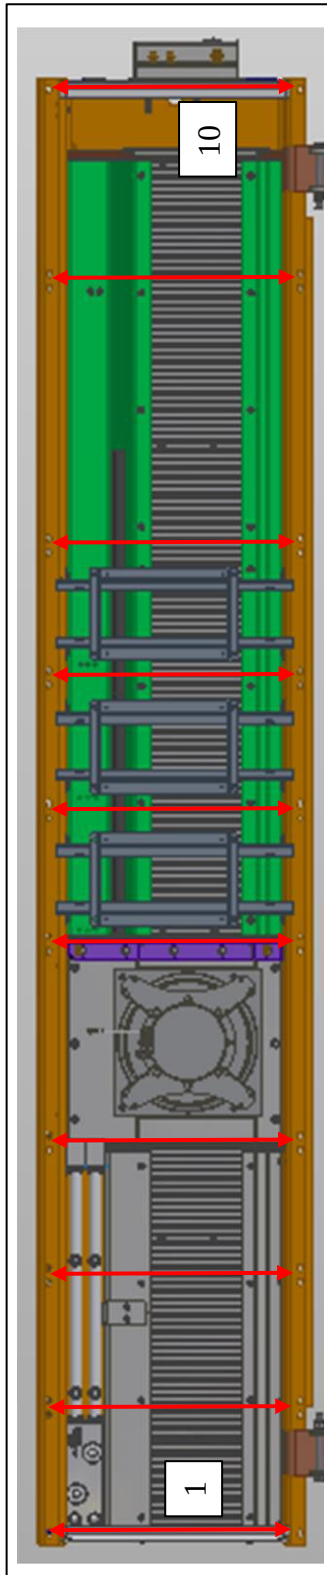

	1	2	3	4	5
	Ok	Ok	Ok	727,4 +/-5	727,4 +/-5
Measure					
Signature					

6	7	8	9	10
727,4 +/-5	Ok	Ok	Ok	Ok

Position 4, 5 and 6 shall be measured and type the actual dimension in table above.

Position 1, 2, 3, 7, 8, 9 and 10 interface holes shall be check with Go / No go tool for verification and set check mark in table above.

The appearance of the fan may vary.

Document Type: Serial Number Registration	Document: SN-1070.0049	Rev. 02	Rev by: DCADA	Rev. date: 2023-12-14
Product: Baseframe Module	Reviewed by: DROKR	Author: DSOLA	Date: 2018-02-16	


1. Purpose of document




Serial no :

This document shall ensure that all necessary components are traceable. This document shall follow the main component through the production line. Following components are marked with individually serial or batch number and have to be written at each row:

Check list:		Initials:	Date:	Check mark:
Assembled.	According to AI-1070.0049, Latest revision.			
Air leak test.	According to TI-1070.0049-1, Latest revision.			
Air Fan test.	According to TI-1070.0049-2, Latest revision.			
Pipe system leak test.	According to TI-1071.0267, Latest revision.			
Interface dimension for cabinet.	According to Appendix COC-1070.0049-1, Latest revision.			
Flatness of Baseframe.	According to Appendix COC-1070.0049-2, Latest revision.			
Part traceability.	According to SN-1070.0049, Latest revision.			
Check for Plugs.	Visual control that pipes and manifolds is plugged.			
Check Seal.	Visual control that seal is attach to fan column in plastic bag.			
Complete inspection.	Visual inspection of complete unit before packed.			
Packing.	According to PI-1070.0049, Latest revision.			


<u>Serial number:</u>	1070.0049 —
------------------------------	--------------------

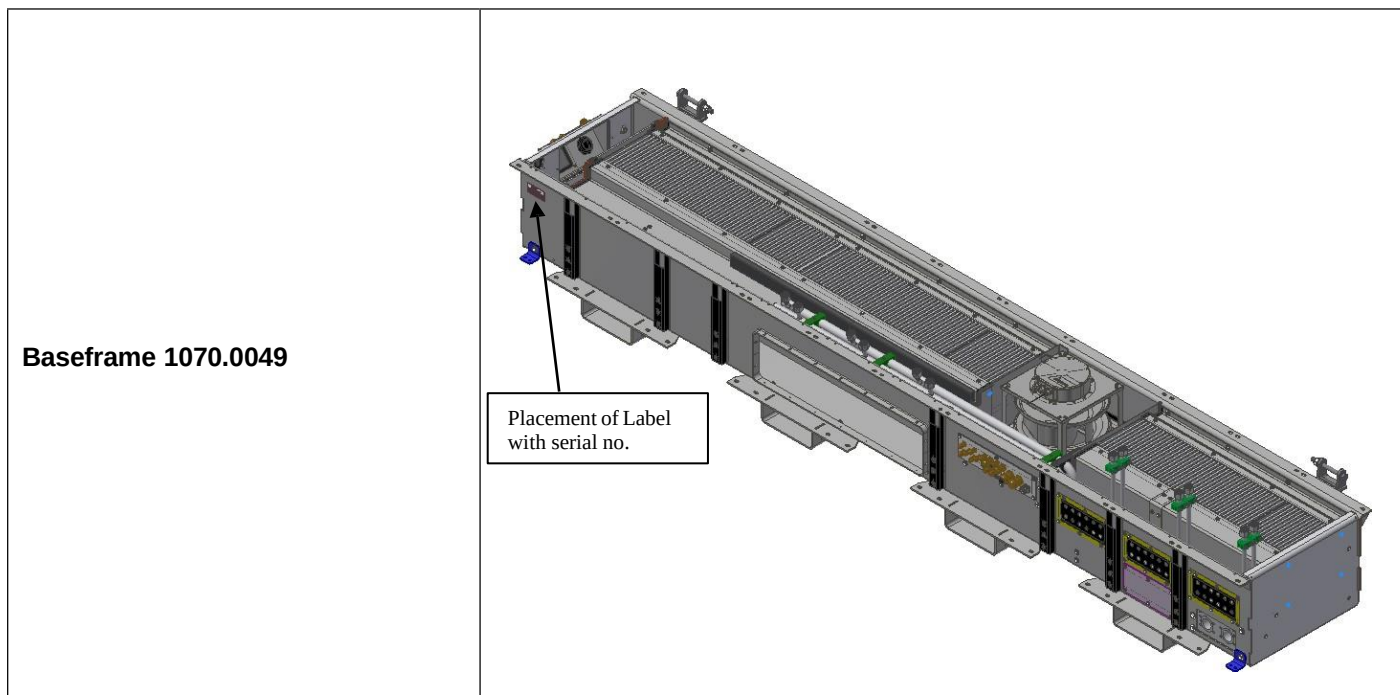

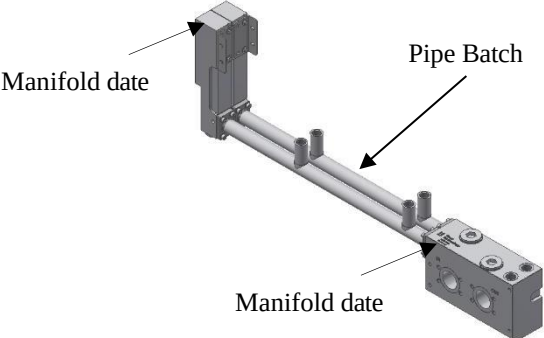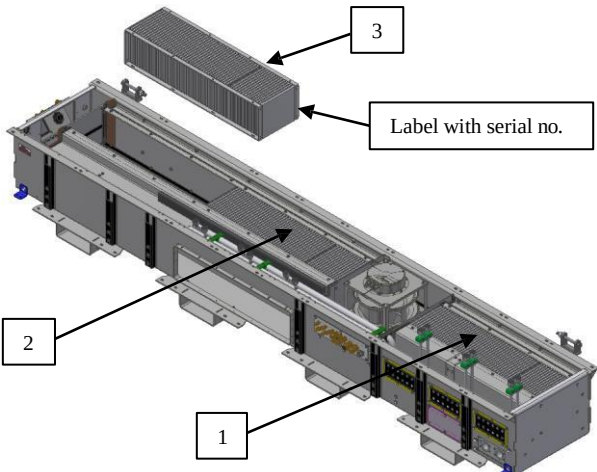Baseframe Weld Assy 3020.1212 Weld Assy. Serial no. = _____	See appendix below for location of serial no.
Fan 1072.0016: Fan serial no. = _____	Label with serial no. 
Cooling System 1071.0267: Batch no.Pipe (9018.0251). = _____ Batch no.Pipe (9018.0251). = _____ Manifold date (7010.0086). = _____ Manifold date (7010.0087). = _____	
Heat exchanger 2080.0002: Heat exchanger 1 serial no. = _____ Heat exchanger 2 serial no. = _____ Heat exchanger 3 serial no. = _____	

Appendix with placement of Serial no. for welded baseframe:

Baseframe Weld Assy. location of serial number:

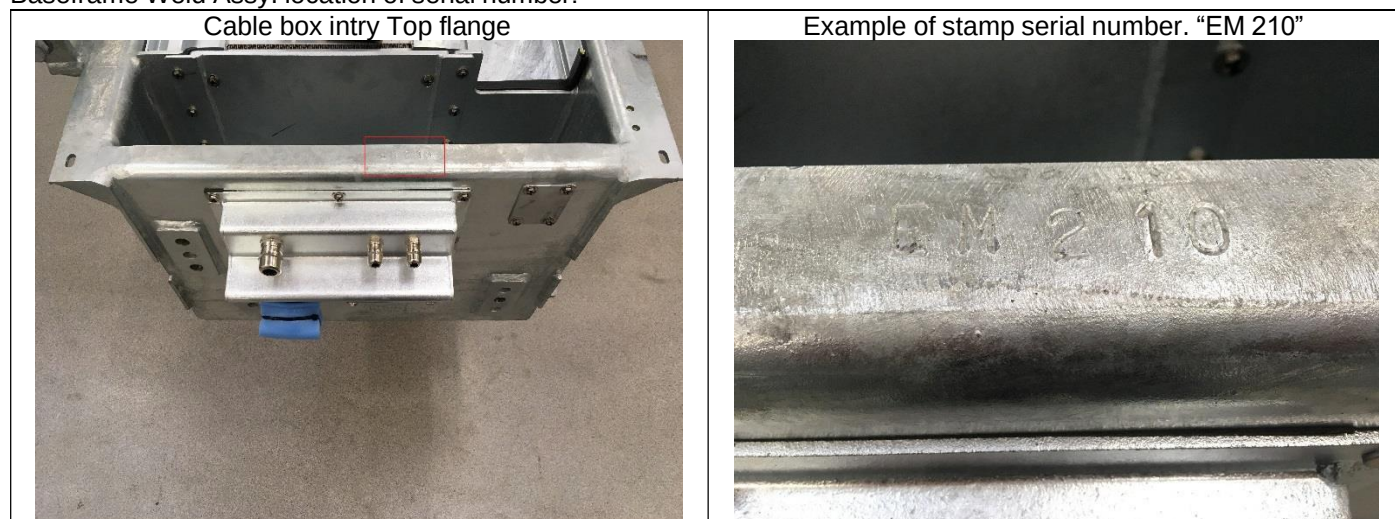

Document Type: Test Instruction	Document: TI-1070.0049-1	Rev. 02	Rev by: DCADA	Rev. date: 2023-12-14
Product: Baseframe module – Air leak test	Reviewed by: DMIAN	Author: DSOLA		Date: 2018-02-19

Baseframe Air leak Test:

Serial no :

Test Procedures:

1. See general equipment manual for setup of test.
(TI-1070.0049-1A).
2. Mount connection plate at front side of baseframe.
3. Mount test equipment to connection plate.
4. Cover all other holes with tape there is free.
5. Switch on test equipment to start the test program.
6. Investigate all sealing joints for leakage and repair them, if there is an opening, where more air comes out than what there will come out of an Ø6 hole.
7. Print out the test result for verification and glue it onto the bottom of this document.
8. Dismount test equipment and small tape pieces.


Results after 5 min. = _____ L/s

Acceptance criteria: Leakage below or equal to 14 L/s within 5 min.

Glue the test result onto this page

Document Type: Test Instruction	Document: TI-1070.0049-2	Rev. 02	Rev by: DCADA	Rev. date: 2023-12-14
Product: Baseframe module – Air fan test	Reviewed by: DMIAN	Author: DSOLA		Date: 2018-02-28

Baseframe Air Fan Test:Serial no :

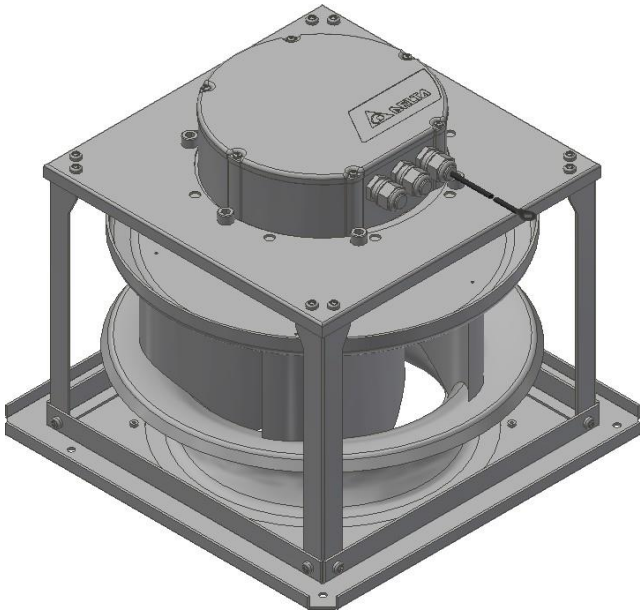**Test Procedures:**

1. Rotate fan by hand and hear if impeller make noise from collision.

Note:

If any unfamiliar noise or collision then shall the fan, be rejected.
