

Document Type: Certificate Of Conformity	Part number: COC-1070.0049	Rev. 02	Rev by: DCADA	Rev. date: 2023-12-14
Product: Baseframe Module	Reviewed by: DROKR	Author: DSOLA	Date: 2018-02-16	

Serial no: **HSIN: 1392**

CERTIFICATE OF CONFORMITY	
Customer Technical Purchase Specification No. and Revision	0068-7211 - Latest version
	0069-2093 - Latest version

HydraSpecma Renewables hereby declare these products have been inspected, tested and, unless otherwise is stated below, conform to purchase order and specifications from Customer.

HSRE part no.	Customer part no.	Description
1070.0049	29107156	Baseframe Module

Customer Purchase order:	POIN010022668
Top level Serial number:	1070.0049 - HSIN: 1392
Manufacturing Order number:	HSIN: 009223

Work flow:	
Assembled.	According to AI-1071.0512 and AI-1070.0049, Latest revision.
Air leak test.	According to TI-1071.0512-1, Latest revision.
Air fan test	According to TI-1071.0512-2, Latest revision.
Interface dimension for cabinet.	According to TI-1071.0512-3, Latest revision.
Flatness of Baseframe.	According to TI-1071.0512-4, Latest revision.
Pipe system Air leak test or Pipe system Helium leak test.	According to TI-1071.0267, Latest revision. According to TI-1071.0267-1, Latest revision.
Part traceability.	According to SN-1070.0049, Latest revision.
Complete inspection.	Visual inspection of complete unit before packed.
Packing.	According to PI-1070.0049, Latest revision.



15.9.26	k. Hemanth sai
Date of Signature	Signature

15.9.26

Document Type: Certificate Of Conformity Appendix	Document: COC-1070.0049-2	Rev. 00	Rev by:	Rev. date: 2023-12-14
Product: Baseframe Module	Reviewed by: DROKR	Author: DSOLA		Date: 2018-02-16

Serial no : **HSIN:1392**


Appendix B: Measure and control flatness of Baseframe after mounting 3020.0919 into 3020.1212

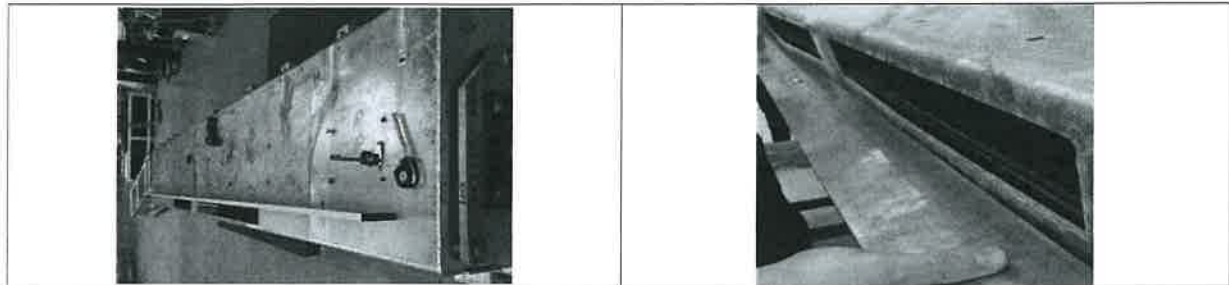

1: Max 4 mm

2: Max 4 mm

3: Max 4 mm

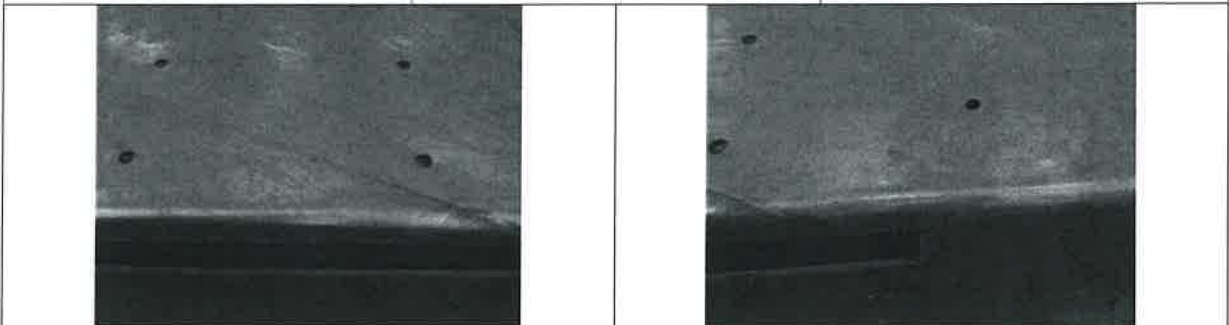

4: Max 4 mm

5: Max 4 mm


1	2	3	4	5
< 1mm	< 1mm	< 2mm	< 1mm	< 1mm

15-9-26

Document Type: Certificate Of Conformity Appendix	Document: COC-1070.0049-1	Rev. 01	Rev by: DCADA	Rev. date: 2023-12-14
Product: Baseframe Module	Reviewed by: DROKR	Author: DSOLA		Date: 2018-02-16

Appendix A.: Interface holes for cabinets.

Serial no: H5IN:1392

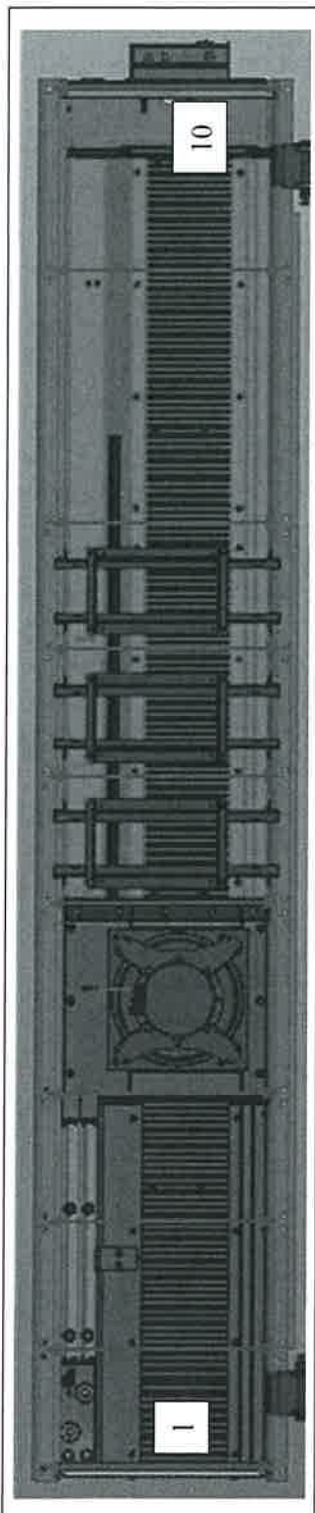

	1	2	3	4	5
	Ok	Ok	Ok	727,4 +/-5	727,4 +/-5
Measure	ok	ok	ok	726	727
Signature	Hemanth	Hemanth	Hemanth	Hemanth	Hemanth

6	7	8	9	10
727,4 +/-5	Ok	Ok	Ok	Ok
728	ok	ok	ok	ok
Hemanth	Hemanth	Hemanth	Hemanth	Hemanth

Position 4, 5 and 6 shall be measured and type the actual dimension in table above.

Position 1, 2, 3, 7, 8, 9 and 10 interface holes shall be check with Go / No go tool for verification and set check mark in table above.

The appearance of the fan may vary.

15-9-26

Document Type: Serial Number Registration	Document: SN-1070.0049	Rev. 02	Rev by: DCADA	Rev. date: 2023-12-14
Product: Baseframe Module	Reviewed by: DROKR	Author: DSOLA	Date: 2018-02-16	


1. Purpose of document

Serial no : **HSIN:1392**

This document shall ensure that all necessary components are traceable. This document shall follow the main component through the production line. Following components are marked with individually serial or batch number and have to be written at each row:



Check list:		Initials:	Date:	Check mark:
Assembled.	According to AI-1070.0049, Latest revision.	Hemanth	15-9-26	✓
Air leak test.	According to TI-1070.0049-1, Latest revision.	"	"	"
Air Fan test.	According to TI-1070.0049-2, Latest revision.	"	"	"
Pipe system leak test.	According to TI-1071.0267, Latest revision.	"	"	"
Interface dimension for cabinet.	According to Appendix COC-1070.0049-1, Latest revision.	"	"	"
Flatness of Baseframe.	According to Appendix COC-1070.0049-2, Latest revision.	"	"	"
Part traceability.	According to SN-1070.0049, Latest revision.	"	"	"
Check for Plugs.	Visual control that pipes and manifolds is plugged.	"	"	"
Check Seal.	Visual control that seal is attach to fan column in plastic bag.	—	—	—
Complete inspection.	Visual inspection of complete unit before packed.	Hemanth	15-9-26	✓
Packing.	According to PI-1070.0049, Latest revision.	"	"	"

Serial number:	1070.0049 — HSIN:1392
-----------------------	------------------------------

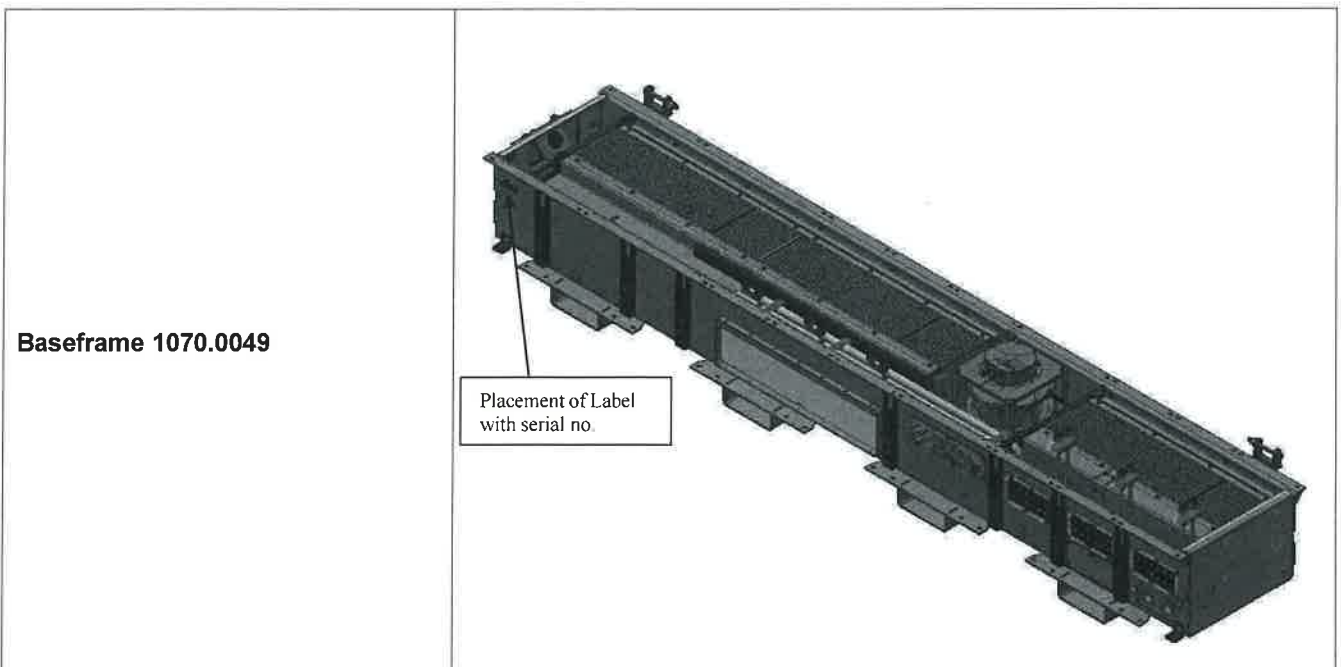

15.9.26


HSIN: 1392

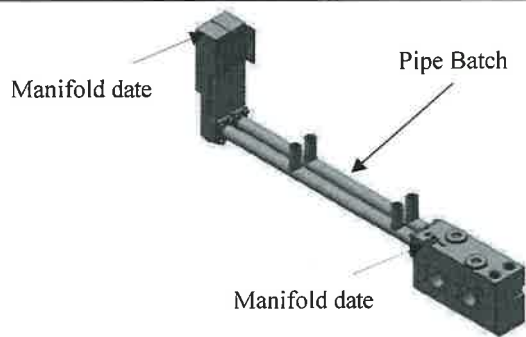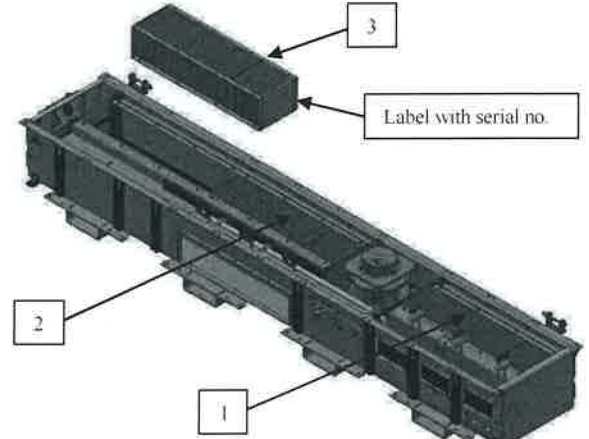Baseframe Weld Assy 3020.1212 Weld Assy. Serial no. = <u> J1438 </u>	See appendix below for location of serial no.
Fan 1072.0016: Fan serial no. = <u> DGD2673000263 </u>	Label with serial no. 
Cooling System 1071.0267: Batch no.Pipe (9018.0251). = <u> 22 26 </u> Batch no.Pipe (9018.0251). = <u> 22 26 </u> Manifold date (7010.0086). = <u> 27.2.26 </u> Manifold date (7010.0087). = <u> 17.3.26 </u>	
Heat exchanger 2080.0002: Heat exchanger 1 serial no. = <u> 260 710 371V </u> Heat exchanger 2 serial no. = <u> 260 710 373V </u> Heat exchanger 3 serial no. = <u> 260 710 372V </u>	

Appendix with placement of Serial no. for welded baseframe:

Baseframe Weld Assy. location of serial number:

Cable box intry Top flange

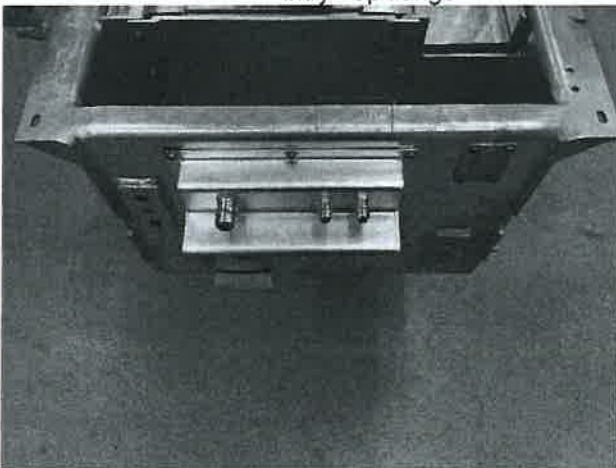

Example of stamp serial number. "EM 210"



15-9-26

Document Type: Test Instruction	Document: TI-1070.0049-1	Rev. 02	Rev by: DCADA	Rev. date: 2023-12-14
Product: Baseframe module – Air leak test	Reviewed by: DMIAN	Author: DSOLA	Date: 2018-02-19	

Baseframe Air leak Test:

Serial no: HS IN: 11392

Test Procedures:

1. See general equipment manual for setup of test. (TI-1070.0049-1A).
2. Mount connection plate at front side of baseframe.
3. Mount test equipment to connection plate.
4. Cover all other holes with tape there is free.
5. Switch on test equipment to start the test program.
6. Investigate all sealing joints for leakage and repair them, if there is an opening, where more air comes out than what there will come out of an Ø6 hole.
7. Print out the test result for verification and glue it onto the bottom of the document.
8. Dismount test equipment and small tape pieces.

Results after 5 min. = 3-8 L/s

Acceptance criteria: Leakage below or equal to 14 L/s within 5 min.

Glue the test result onto this page

HS IN 11392
HYDRA SPECMA
LEAKAGE TEST

**** Lindab LT600 ****
Serial number 631
Version 1.18

Test report ID# 5111

Leakage test report of
air ducts in accordance
with EN 12237, EN 1507,
EN 12599, EN 16798-3
and EN 1366-8

Test object information

Surface area : 8.70 m²
Tightness cl : U
Rate factor
RF: 20.8698 l/s 1/m²
Adapter type: w/o
Pressure : 800.0Pa

Testpressure: 802.8Pa
Leakage rate: 3.83l/s
Endurance : 300 sec

Limit ATC6 : 45.38
Limit ATC5 (A): 18.15
Limit ATC4 (B): 6.05
Limit ATC3 (C): 2.02
Limit ATC2 (D): 0.67
Limit ATC1 : 0.22
Limit U : 14.03

Result:

Test object TEST PASSED

Date: 15.09.2026

Time: 11:23


Signature:

15-9-26

Document Type: Test Instruction	Document: TI-1070.0049-2	Rev. 02	Rev by: DCADA	Rev. date: 2023-12-14
Product: Baseframe module – Air fan test	Reviewed by: DMIAN	Author: DSOLA		Date: 2018-02-28

Baseframe Air Fan Test:

Serial no : **HSIN11392**

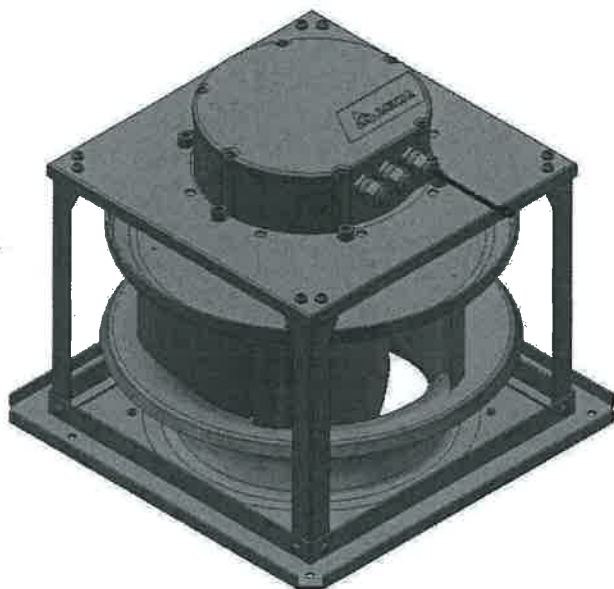

Test Procedures:

1. Rotate fan by hand and hear if impeller make noise from collision.


N:1

Note:

If any unfamiliar noise or collision then shall the fan, be rejected.

Document Type: Test Instruction	Document: TI-1071.0267	Rev. 00	Rev by:	Rev. date:
Product: Baseframe module – Pipe system leak test	Reviewed by: DROKR	Author: DSOLA	Date: 2018-02-19	

Test of Pipe system: **56**

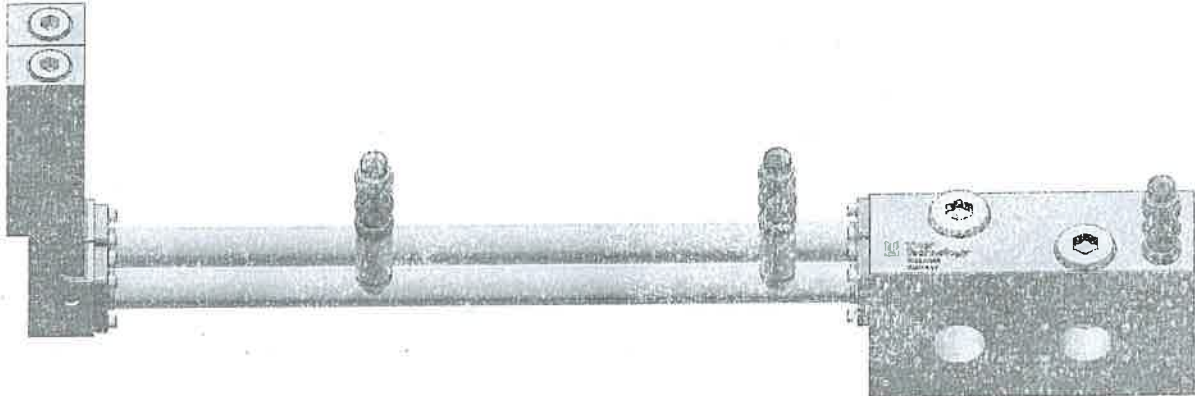

Test Procedures:

1. See general equipment manual for setup of test. (TI-1071.0267-A).
2. Mount Plugs 3/4" BSPP at pipe sockets ends for test and block openings.
3. Mount test equipment to manifold.
4. Pressurize the system to 5,6 bar (+ 0.1 / - 0 bar) and let it stabilize for 20 min. before test start.
5. Reduce the pressure to 5,35 - 5,45 bar.
6. Note end pressure after 60 min. and calculate if there is an pressure drop more than 0,05 Bar.
7. Depressurize the system.
8. Dismount test equipment and mount plastic plugs.

INLET:

Inlet Pressure Start Of Test = 5.44 Bar

Inlet Pressure End Of Test after 60 min = 5.44 Bar

Calculate Pressure drop below or equal $\leq 0,05$ = 0.00 Bar

OUTLET:

Outlet Pressure start Of Test = 5.45 Bar

Outlet Pressure End Of Test after 60 min = 5.45 Bar

Calculate Pressure drop below or equal $\leq 0,05$ = 0.00 Bar

Acceptance criteria: No pressure drop more than 0,05 bar from start pressure within 60 min.

Signature: B. Bhargath Raj Date: 11/09/2026
